



Project Status Report No.1

Wheatland – Chili Central School District

Capital Project Phase I

C&S Project Number –U92001001

Client Contact – Deborah Leh

Enter Period (June 25 - July 20 2018)

Significant activities underway or completed this period:

- ✓ Pre-construction Meeting
- ✓ Contracts Executed
- ✓ Submittal Process Executed
- ✓ Mobilization of GC Kuitems Construction
- ✓ Staging Area in place
- ✓ Progress & Coordination Meeting #1
- ✓ Bleacher removal completed
- ✓ Soffit and Partition Wall removal completed
- ✓ Wall padding removal completed
- ✓ Electrical disconnects completed

Next period's expected activities:

- ✓ Removal of existing ceramic wall tile and backer board
- ✓ Painting of roof structure including trusses, cross bracing, roof deck, etc.
- ✓ Installation of acoustical ceiling panels
- ✓ Removal of existing gym floor
- ✓ Relocation of existing backboard and accessories

Other important project information:

- ✓ **Gym Floor installation schedule for the 1st week of September.**
- ✓ **Future Progress Meeting to be held in athletic office adjacent to the gym.**
- ✓ **Security camera located on exterior of north gym wall has been disconnected as part of electrical disconnect. It will be reconnected as part of electrical work.**

Information/direction needed from client:

- ✓ Gym Floor Logo – Cannot be removed in one piece
- ✓

Project Status Report No.1

Contractor Staging Area:



Project Status Report No.1

Bleacher Removal:

South Wall – East half of gym



South Wall – West half of gym



Project Status Report No.1

North Wall – East half of gym




North Wall – West half of gym



Project Status Report No.1

Soffit Removal:

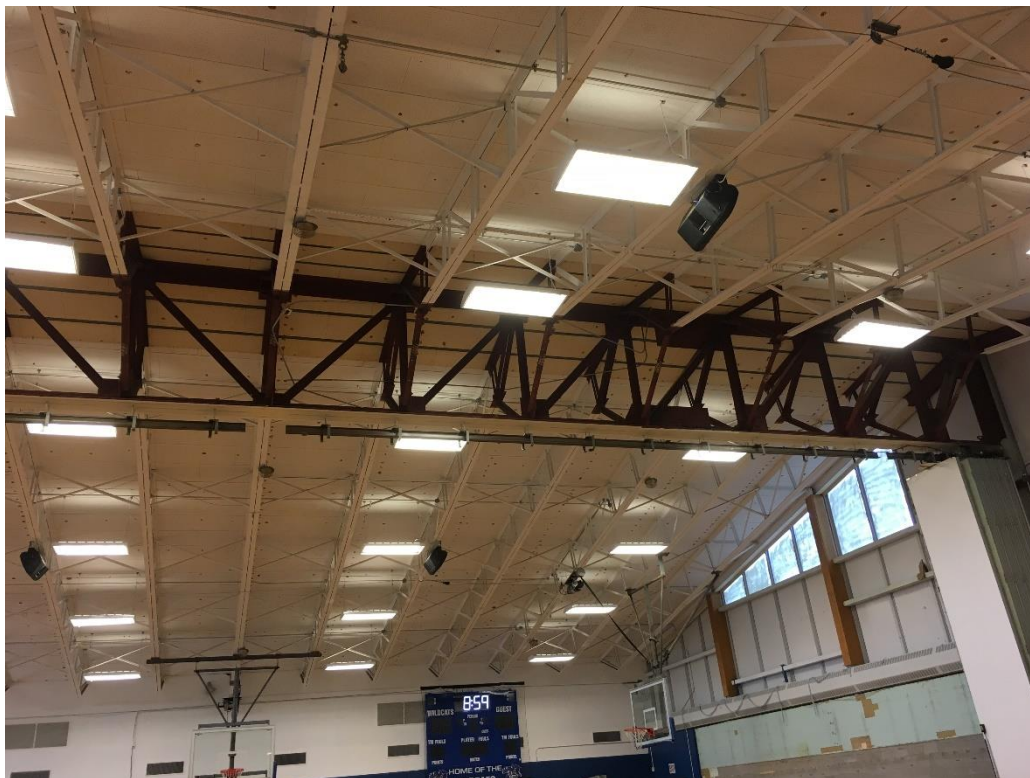

Project Status Report No.1

Partition Wall Removal:



Project Status Report No.1

Wall Padding Removal:

East Wall



West Wall

