

## PROJECT STATUS REPORT

### Wheatland-Chili Central School District

### 2017 Capital Improvement Project

C&S Project # - U92001001

Client Contact – Deborah Leh

May 2020

#### Phase II - To date:

- Northeastern Electrical completed all work, pay app has been submitted.
- Crosby-Brownlie waiting for TJ boilers to be drained to complete commissioning work.
- Horizon Engineering to complete final commissioning checklist.

#### Phase III update:

- All prime contractors have mobilized and have begun work.
- Materials and equipment being ordered for boiler rooms.
- All boiler piping and breeching has been demoed at the High School by Bell Mechanical.
- Gas supply and venting has been demoed by Landry Mechanical in boiler rooms at both schools.
- All power has been removed from boilers, pumps, and drives at the High School boiler room by Concord Electric.
- Day Automation has demoed all controls for boiler rooms at the High school.
- Abatement of exterior caulking is ongoing at TJ by Sessler Environmental.
- Landry Mechanical removed sinks, urinals, and toilets removed from TJ locker rooms.
- Excavation and sub-base stone was installed for main side walk at TJ Connor.
- Trenching was completed and conduit was installed for charging stations at TJ.
- Concrete was poured for duct bank to charging stations, all trenching was backfilled.

#### Phase II – Upcoming construction:

- Closeout of remaining contracts.


#### Phase III – Upcoming dates:

- Bus garage mechanical upgrades 6/1
- TJ Connor boiler room demo 6/19
- Bus garage lift anticipating arrival in July from state contract.



## PROJECT STATUS REPORT

### TJ Connor Elementary

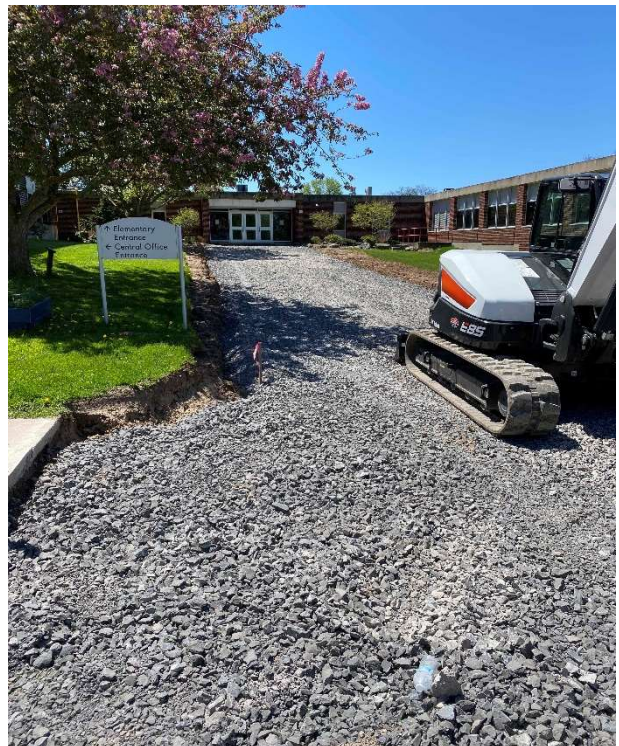



## PROJECT STATUS REPORT

High School

