

PROJECT STATUS REPORT No. 3

Wheatland-Chili Central School District

2018 Capital Project Phase I

C&S Project # - U92001001

Client Contact – Deborah Leh

Enter Period (September 1st 2018)

Significant activities underway or completed this period

- Asbestos abatement and gym floor removal at TJ Connor Elementary School
- Miscellaneous electrical (fasten conduits to wall, reattach receptacles and boxes, etc.)
- Installed metal angles and hollow steel for basketball backboard relocation
- Installed hat channel aluminum for acoustical ceiling panels
- Painting of the roof joists and cross bracing within HS, color Blue Blood

Next period's expected activities:


- Finish painting existing roof deck and walls and miscellaneous touch-up work
- Install new acoustical ceiling in high school gym
- Relocate basketball backboards
- Remove existing gym floor
- Install new gym floor
- Install new bleachers

Other Important project information:

- Continued coordination between trades and the school district will be needed to keep work going steadily
- Contractor will do their best to remove the existing gym floor logo

PROJECT STATUS REPORT No. 3

High School/Middle School Gym

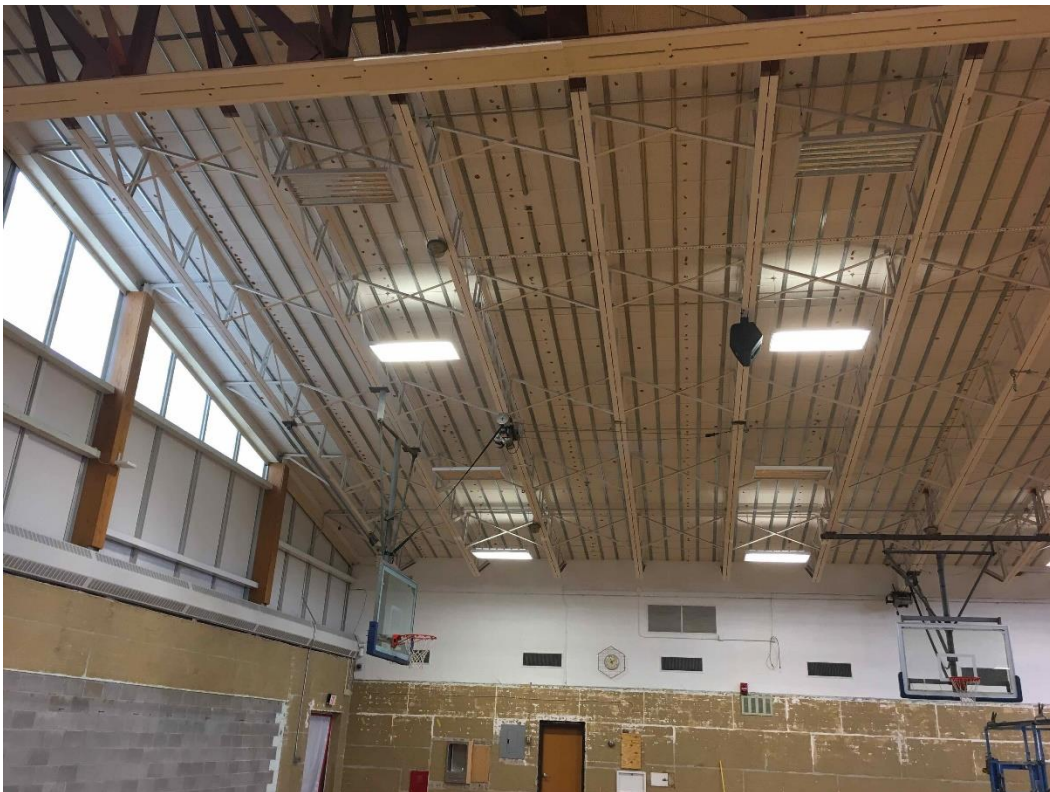

PROJECT STATUS REPORT No. 3



TJ Connor Elementary Gym



PROJECT STATUS REPORT No. 3

